

Project Proposal

Date: 19th November 2025
For: MRFQ
From: Prince Malani

Project: Corporate Website Design & Development

Project Overview

This proposal outlines the design and development of a modern, high-performance website for **MRFQ**, aligned with your SaaS brand identity and user expectations. The website will be built using **React.js**, ensuring speed, scalability, and a smooth user experience. The design direction will draw inspiration from the provided references while maintaining a clean, futuristic aesthetic and strong visual storytelling.

Key visual principles include:

- Dynamic visual style based on the shared video reference.
- Modern SaaS UI inspiration from **AimFox**.
- Brand-based color themes, typography, and structure.
- **3D scenes and illustrations** tailored to your product.

Project Scope

1. Website Development (React.js)

The website will be developed using **React.js** with a modular, scalable component architecture, ensuring high performance and easy future updates.

2. UI/UX Design (Figma)

A complete design system and landing page UI will be created in Figma based on your brand identity, including:

- Landing page
- All major sections
- Custom 3D scenes (as requested)


3. Development Support

A **15-day support period** is included post-deployment.

4. Reference Projects by Syntra Softwares

1. <https://a1ecommerceexpert.com/> – High-performance landing page and SaaS-style storytelling.
2. <https://hypertarget.app/>
A multilingual website (available in 3 languages) showcasing dynamic UI, clean layout, and optimized performance.

3. Aaradhya Design Gallery

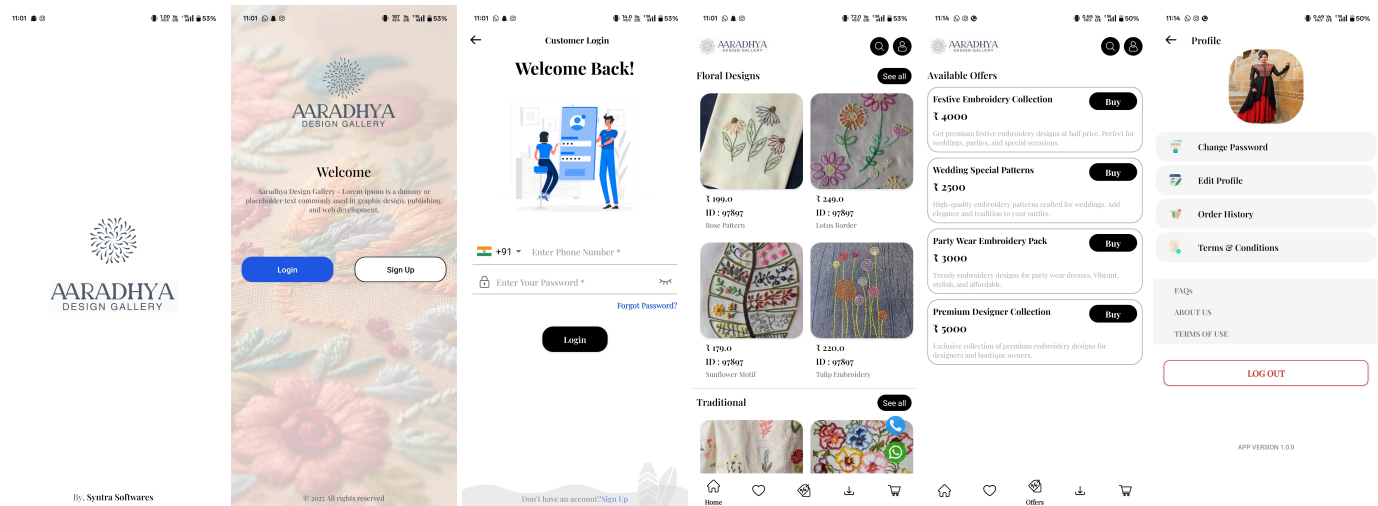

Features Included

- ✓ Mobile-Responsive Design
- ✓ Performance Optimization
- ✓ Basic SEO Setup
- ✓ 3D Scene Creation
- ✓ 3 Revision Rounds for Figma
- ✓ 3 Revision Rounds for Development

Project Timeline (10 Weeks)

Week	Deliverables
Week 1	Requirement confirmation, brand identity briefing, & flow finalisation
Week 2	Wireframes, design moodboard, 3D concept direction
Week 3	Figma design
Week 4	Figma design
Week 5	Final design revisions + approval
Week 6	React.js structure setup, components architecture
Week 7	Core landing page development (UI build-out)
Week 8	Integrating animations, transitions & 3D scenes
Week 9	SEO setup, performance optimization, QA
Week 10	Final testing, deployment, handover & support initiation

Cost Breakdown

Component	Estimated Cost
Website Development (React.js)	₹95,000 – ₹1,05,000
UI/UX Figma Design	₹22,000 – ₹28,000
Deployment & Hosting Setup	₹10,000 – ₹15,000
3D Scene Creation	₹10,000 – ₹15,000
15-Day Development Support	Included

Total Estimated Cost: ₹1,37,000 – ₹1,63,000 INR

Payment Schedule

Milestone	Payment %	Amount (Approx.)
Project Start (Advance)	40%	₹54,800 – ₹65,200
Live Preview + Revision Stage	40%	₹54,800 – ₹65,200
Final Delivery & Handover	20%	₹27,400 – ₹32,600

Deliverables

- Complete **React.js** codebase
- GitHub repository with full documentation
- Figma design file (all screens)
- 3D scenes and assets
- Deployment setup (server, SSL, domain configuration)

- Basic SEO setup
 - Performance optimisation
 - 15 days support post launch
 - Technical documentation for maintenance
-

Legal Note

This proposal is confidential and intended exclusively for **MRFQ**.

Sharing, distributing, or using this document without permission from **Syntra Softwares** may lead to legal consequences.

Additional Note

Further changes to the project scope or new requirements **may increase or decrease the overall project cost** based on the nature and volume of additional work.

Acceptance

If this proposal meets your expectations, we can proceed toward the formal agreement and project initiation.

Thank you for choosing us.
